	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names
1		**Week 1**	**5 days**	**Mon 5/4/26**	**Fri 5/8/26**	**5**	
2		Site verification of existing	2 days	Mon 5/4/26 8:00 AM	Tue 5/5/26 5:00 PM	5;	
3		Create floor verification plan	2 days	Mon 5/4/26 8:00 AM	Tue 5/5/26 5:00 PM	2SS	
4		Level or grind floor as required	3 days	Wed 5/6/26 8:00 AM	Fri 5/8/26 5:00 PM	3	
5		**Week 2**	**5 days**	**Mon 5/11/2**	**Fri 5/15/26**		
6		Complete	2 days	Mon 5/11/26 8:00 AM	Tue 5/12/26 5:00 PM	4	
7		Store layout	2 days	Thu 5/14/26 8:00 AM	Fri 5/15/26 5:00 PM	6FS+1 day	
8		**Week 3**	**5 days**	**Mon 5/18/2**	**Fri 5/22/26**		
9		HVAC rough	5 days	Mon 5/18/26 8:00 AM	Fri 5/22/26 5:00 PM	7	
10		Storefront heavy gauge framing	5 days	Mon 5/18/26 8:00 AM	Fri 5/22/26 5:00 PM	9SS	
11		Electrical/	5 days	Mon 5/18/26 8:00 AM	Fri 5/22/26 5:00 PM	9SS	
12		**Week 4**	**5 days**	**Mon 5/25/2**	**Fri 5/29/26**		
13		Air handler delivery and	2 days	Mon 5/25/26 8:00 AM	Tue 5/26/26 5:00 PM	11	
14		HVAC rough	5 days	Mon 5/25/26 8:00 AM	Fri 5/29/26 5:00 PM	13SS	
15		Electrical/	5 days	Mon 5/25/26 8:00 AM	Fri 5/29/26 5:00 PM	14SS	
16		Wall framing/ blocking	5 days	Mon 5/25/26 8:00 AM	Fri 5/29/26 5:00 PM	5;	
17		Scan and trench	1 day	Wed 5/27/26 8:00 AM	Wed 5/27/26 5:00 PM	15SS+2 days	
18		Plumbing rough	2 days	Thu 5/28/26 8:00 AM	Fri 5/29/26 5:00 PM	17	
19		**Week 5**	**4 days**	**Tue 6/2/26**	**Fri 6/5/26**	**5**	
20		Delivery of Light troughs	0 days	Tue 6/2/26 12:00 AM	Tue 6/2/26 12:00 AM	18FS+1 day	
21		Delivery and install of	0 days	Tue 6/2/26 12:00 AM	Tue 6/2/26 12:00 AM	20	
22		Framing/	4 days	Tue 6/2/26 8:00 AM	Fri 6/5/26 5:00 PM	21SS	
23		HVAC rough	4 days	Tue 6/2/26 8:00 AM	Fri 6/5/26 5:00 PM	22SS	
24		Electrical/	4 days	Tue 6/2/26 8:00 AM	Fri 6/5/26 5:00 PM	23SS	
25		Plumbing rough	4 days	Tue 6/2/26 8:00 AM	Fri 6/5/26 5:00 PM	23SS	
26		Sprinkler rough	4 days	Tue 6/2/26 8:00 AM	Fri 6/5/26 5:00 PM	24SS	
27		FA rough	4 days	Tue 6/2/26 8:00 AM	Fri 6/5/26 5:00 PM	26SS	
28		Trench rough inspection	2 days	Thu 6/4/26 8:00 AM	Fri 6/5/26 5:00 PM	25SS+2 days	
29		Trench infill	1 day	Fri 6/5/26 8:00 AM	Fri 6/5/26 5:00 PM	28SS+1 day	
30		**Week 6**	**4 days**	**Tue 6/9/26**	**Sat 6/13/26**		
31		Framing/	4 days	Tue 6/9/26 8:00 AM	Fri 6/12/26 5:00 PM	29FS+1 day	
32		HVAC rough	4 days	Tue 6/9/26 8:00 AM	Fri 6/12/26 5:00 PM	31SS	
33		Electrical/	4 days	Tue 6/9/26 8:00 AM	Fri 6/12/26 5:00 PM	32SS	
34		Sprinkler rough	4 days	Tue 6/9/26 8:00 AM	Fri 6/12/26 5:00 PM	33SS	
35		FA rough	4 days	Tue 6/9/26 8:00 AM	Fri 6/12/26 5:00 PM	34SS	
36		Delivery of Smart Meter	0 days	Sat 6/13/26 12:00 AM	Sat 6/13/26 12:00 AM	35FF	
37		**Week 7**	**4 days**	**Tue 6/16/2**	**Fri 6/19/26**		
38		Framing/	4 days	Tue 6/16/26 8:00 AM	Fri 6/19/26 5:00 PM	36FS+1 day	
39		HVAC rough	4 days	Tue 6/16/26 8:00 AM	Fri 6/19/26 5:00 PM	38SS	
40		Electrical/	4 days	Tue 6/16/26 8:00 AM	Fri 6/19/26 5:00 PM	39SS	
41		Sprinkler rough	4 days	Tue 6/16/26 8:00 AM	Fri 6/19/26 5:00 PM	40SS	
42		FA rough	4 days	Tue 6/16/26 8:00 AM	Fri 6/19/26 5:00 PM	41SS	
43		**Week 8**	**4 days**	**Mon 6/22/2**	**Fri 6/26/26**		
44		MEP rough inspections	2 days	Mon 6/22/26 8:00 AM	Tue 6/23/26 5:00 PM	42	
45		Framing/	4 days	Mon 6/22/26 8:00 AM	Thu 6/25/26 5:00 PM	44SS	
46		HVAC balance	1 day	Wed 6/24/26 8:00 AM	Wed 6/24/26 5:00 PM	44	
47		Framing	0 days	Fri 6/26/26 8:00 AM	Fri 6/26/26 8:00 AM	44	
48		**Week 9**	**4 days**	**Mon 6/29/2**	**Fri 7/3/26**	**1**	
49		Drywall install on walls	4 days	Mon 6/29/26 8:00 AM	Thu 7/2/26 5:00 PM	47FS+1 day	
50		Level 5 drywall sample	0 days	Fri 7/3/26 12:00 AM	Fri 7/3/26 12:00 AM	49	
51		Delivery of knife edge cover	0 days	Fri 7/3/26 12:00 AM	Fri 7/3/26 12:00 AM	49FF	
52		**Week 10**	**4 days**	**Tue 7/7/26**	**Fri 7/10/26**		
53		Drywall on walls and ceilings	4 days	Tue 7/7/26 8:00 AM	Fri 7/10/26 5:00 PM	51FS+2 days	
54		**Week 11**	**4 days**	**Tue 7/14/2**	**Fri 7/17/26**		
55		Drywall finishing	4 days	Tue 7/14/26 8:00 AM	Fri 7/17/26 5:00 PM	53FS+1 day	
56		**Week 12**	**4 days**	**Tue 7/21/2**	**Sat 7/25/26**		
57		Drywall	4 days	Tue 7/21/26 8:00 AM	Fri 7/24/26 5:00 PM	55FS+1 day	
58		Delivery of Rasalite tile	0 days	Sat 7/25/26 2:00 AM	Sat 7/25/26 2:00 AM	57FF	
59		**Week 13**	**4 days**	**Tue 7/28/2**	**Sat 8/1/26**		
60		Storefront installation	4 days	Tue 7/28/26 2:00 AM	Fri 7/31/26 5:00 PM	58FS+1 day	
61		Interior paint and prime	4 days	Tue 7/28/26 2:00 AM	Fri 7/31/26 5:00 PM	60SS	
62		Install interior HM doors	3 days	Wed 7/29/26 12:00 AM	Fri 7/31/26 5:00 PM	61FS-3 days	
63		Dry layout of FOH tile with	0 days	Sat 8/1/26 12:00 AM	Sat 8/1/26 12:00 AM	62FF-1 days	
64		**Week 14**	**4 days**	**Tue 8/4/26**	**Fri 8/7/26**	**5**	
65		Storefront installation	4 days	Tue 8/4/26 12:00 AM	Fri 8/7/26 5:00 PM	63FS+1 day	
66		Interior paint and prime	4 days	Tue 8/4/26 12:00 AM	Fri 8/7/26 5:00 PM	65SS	
67		Install BOH ACT ceilings	0 days	Fri 8/7/26 8:00 AM	Fri 8/7/26 8:00 AM	66FS-2 days	
68		**Week 15**	**5 days**	**Mon 8/10/2**	**Fri 8/14/26**		
69		FOH tile	5 days	Mon 8/10/26 8:00 AM	Fri 8/14/26 5:00 PM	67FS+1 day	
70		**Week 16**	**5 days**	**Mon 8/17/2**	**Sat 8/22/26**		
71		FOH tile	5 days	Mon 8/17/26 8:00 AM	Fri 8/21/26 5:00 PM	69	
72		Install Floor protection	1 day	Fri 8/21/26 8:00 AM	Fri 8/21/26 5:00 PM	71FF	
73		Reverse ceiling and floor light	0 days	Sat 8/22/26 2:00 AM	Sat 8/22/26 2:00 AM	72FF	
74		**Week 17**	**4 days**	**Tue 8/25/2**	**Fri 8/28/26**		
75		Storefront facade install	4 days	Tue 8/25/26 12:00 AM	Fri 8/28/26 5:00 PM	73FS+1 day	
76		Millwork	4 days	Tue 8/25/26 12:00 AM	Fri 8/28/26 5:00 PM	75SS	
77		**Week 18**	**4 days**	**Tue 9/1/26**	**Fri 9/4/26**	**5**	
78		Millwork	4 days	Tue 9/1/26 8:00 AM	Fri 9/4/26 5:00 PM	76FS+1 day	
79		Millwork	4 days	Tue 9/1/26 8:00 AM	Fri 9/4/26 5:00 PM	78SS	
80		**Week 19**	**4 days**	**Tue 9/8/26**	**Sat 9/12/26**		
81		Storefront facade install	4 days	Tue 9/8/26 8:00 AM	Fri 9/11/26 5:00 PM	79FS+1 day	
82		Millwork	4 days	Tue 9/8/26 8:00 AM	Fri 9/11/26 5:00 PM	81SS	
83		Electrical	4 days	Tue 9/8/26 8:00 AM	Fri 9/11/26 5:00 PM	82SS	
84		BOH Millwork	4 days	Tue 9/8/26 8:00 AM	Fri 9/11/26 5:00 PM	83SS	
85		Delivery of LV rack, WAPS, Ect	0 days	Sat 9/12/26 2:00 AM	Sat 9/12/26 2:00 AM	84FF	
86		**Week 20**	**4 days**	**Tue 9/15/2**	**Fri 9/18/26**		
87		Millwork	4 days	Tue 9/15/26 8:00 AM	Fri 9/18/26 5:00 PM	85FS+1 day	
88		Electrical	4 days	Tue 9/15/26 8:00 AM	Fri 9/18/26 5:00 PM	87SS	
89		Delivery and install of Mobile	2 days	Thu 9/17/26 2:00 AM	Fri 9/18/26 5:00 PM	88SS+2 days	
90		Delivery of BOH appliances	3 days	Wed 9/16/26 12:00 AM	Fri 9/18/26 5:00 PM	89FF	
91		**Week 21**	**4 days**	**Tue 9/22/2**	**Sat 9/26/26**		
92		Millwork	4 days	Tue 9/22/26 8:00 AM	Fri 9/25/26 5:00 PM	90FS+1 day	
93		Electrical	4 days	Tue 9/22/26 8:00 AM	Fri 9/25/26 5:00 PM	92SS	
94		Delivery of safe	0 days	Sat 9/26/26 2:00 AM	Sat 9/26/26 2:00 AM	93FF	
95		Delivery of People Counter	0 days	Sat 9/26/26 2:00 AM	Sat 9/26/26 2:00 AM	93FF	
96		Delivery of EAS/security	0 days	Sat 9/26/26 2:00 AM	Sat 9/26/26 2:00 AM	93FF	
97		**Week 22**	**4 days**	**Tue 9/29/2**	**Fri 10/2/26**		
98		Millwork Punch	4 days	Tue 9/29/26 8:00 AM	Fri 10/2/26 5:00 PM	96FS+1 day	
99		Electrical	4 days	Tue 9/29/26 8:00 AM	Fri 10/2/26 5:00 PM	98SS	
100		IT installation	4 days	Tue 9/29/26 8:00 AM	Fri 10/2/26 5:00 PM	99SS	
101		Audio install	4 days	Tue 9/29/26 8:00 AM	Fri 10/2/26 5:00 PM	100SS	
102		Security install	4 days	Tue 9/29/26 8:00 AM	Fri 10/2/26 5:00 PM	101SS	
103		Plumbing fit out	4 days	Tue 9/29/26 8:00 AM	Fri 10/2/26 5:00 PM	101SS	
104		Sprinkler fit out	4 days	Tue 9/29/26 8:00 AM	Fri 10/2/26 5:00 PM	101SS	
105		Intertek	1 day	Fri 10/2/26 12:00 AM	Fri 10/2/26 5:00 PM	104SS+3 days	
106		**Week 23**	**4 days**	**Tue 10/6/2**	**Sat 10/10/2**		
107		Final Paint	2 days	Tue 10/6/26 8:00 AM	Wed 10/7/26 5:00 PM	105FS+1 day	
108		GC punch visit	1 day	Tue 10/6/26 8:00 AM	Tue 10/6/26 5:00 PM	107SS	
109		GC punch	3 days	Wed 10/7/26 8:00 AM	Fri 10/9/26 5:00 PM	108	
110		Final Clean #1	2 days	Thu 10/8/26 8:00 AM	Fri 10/9/26 5:00 PM	107	
111		Exterior signage installation	2 days	Thu 10/8/26 2:00 AM	Fri 10/9/26 5:00 PM	110SS	
112		MEP final	0 days	Sat 10/10/26 2:00 AM	Sat 10/10/26 2:00 AM	111	
113		Signage	0 days	Sat 10/10/26 2:00 AM	Sat 10/10/26 2:00 AM	112SS+1 day	
114		**Week 24**	**4 days**	**Tue 10/13/**	**Sat 10/17/2**		
115		Life Safety Inspection	0 days	Tue 10/13/26 12:00 AM	Tue 10/13/26 12:00 AM	113FS+1 day	
116		Final Building inspection	0 days	Wed 10/14/26 12:00 AM	Wed 10/14/26 12:00 AM	115FS+1 day	
117		Final Clean #2	2 days	Thu 10/15/26 8:00 AM	Fri 10/16/26 5:00 PM	116FS+1 day	
118		Client turnover	0 days	Sat 10/17/26 2:00 AM	Sat 10/17/26 2:00 AM	117	
119		**Week 25**	**4 days**	**Tue 10/20/**	**Sat 10/24/2**		
120		Stock Store	4 days	Tue 10/20/26 8:00 AM	Fri 10/23/26 5:00 PM	118FS+1 day	
121		Install	1 day	Tue 10/20/26 8:00 AM	Tue 10/20/26 5:00 PM	120SS	
122		Remove	1 day	Fri 10/23/26 8:00 AM	Fri 10/23/26 5:00 PM	120FF	
123		Touch up for barricade	1 day	Fri 10/23/26 2:00 AM	Fri 10/23/26 5:00 PM	122SS	
124		Store Opening	0 days	Sat 10/24/26 2:00 AM	Sat 10/24/26 2:00 AM	123	

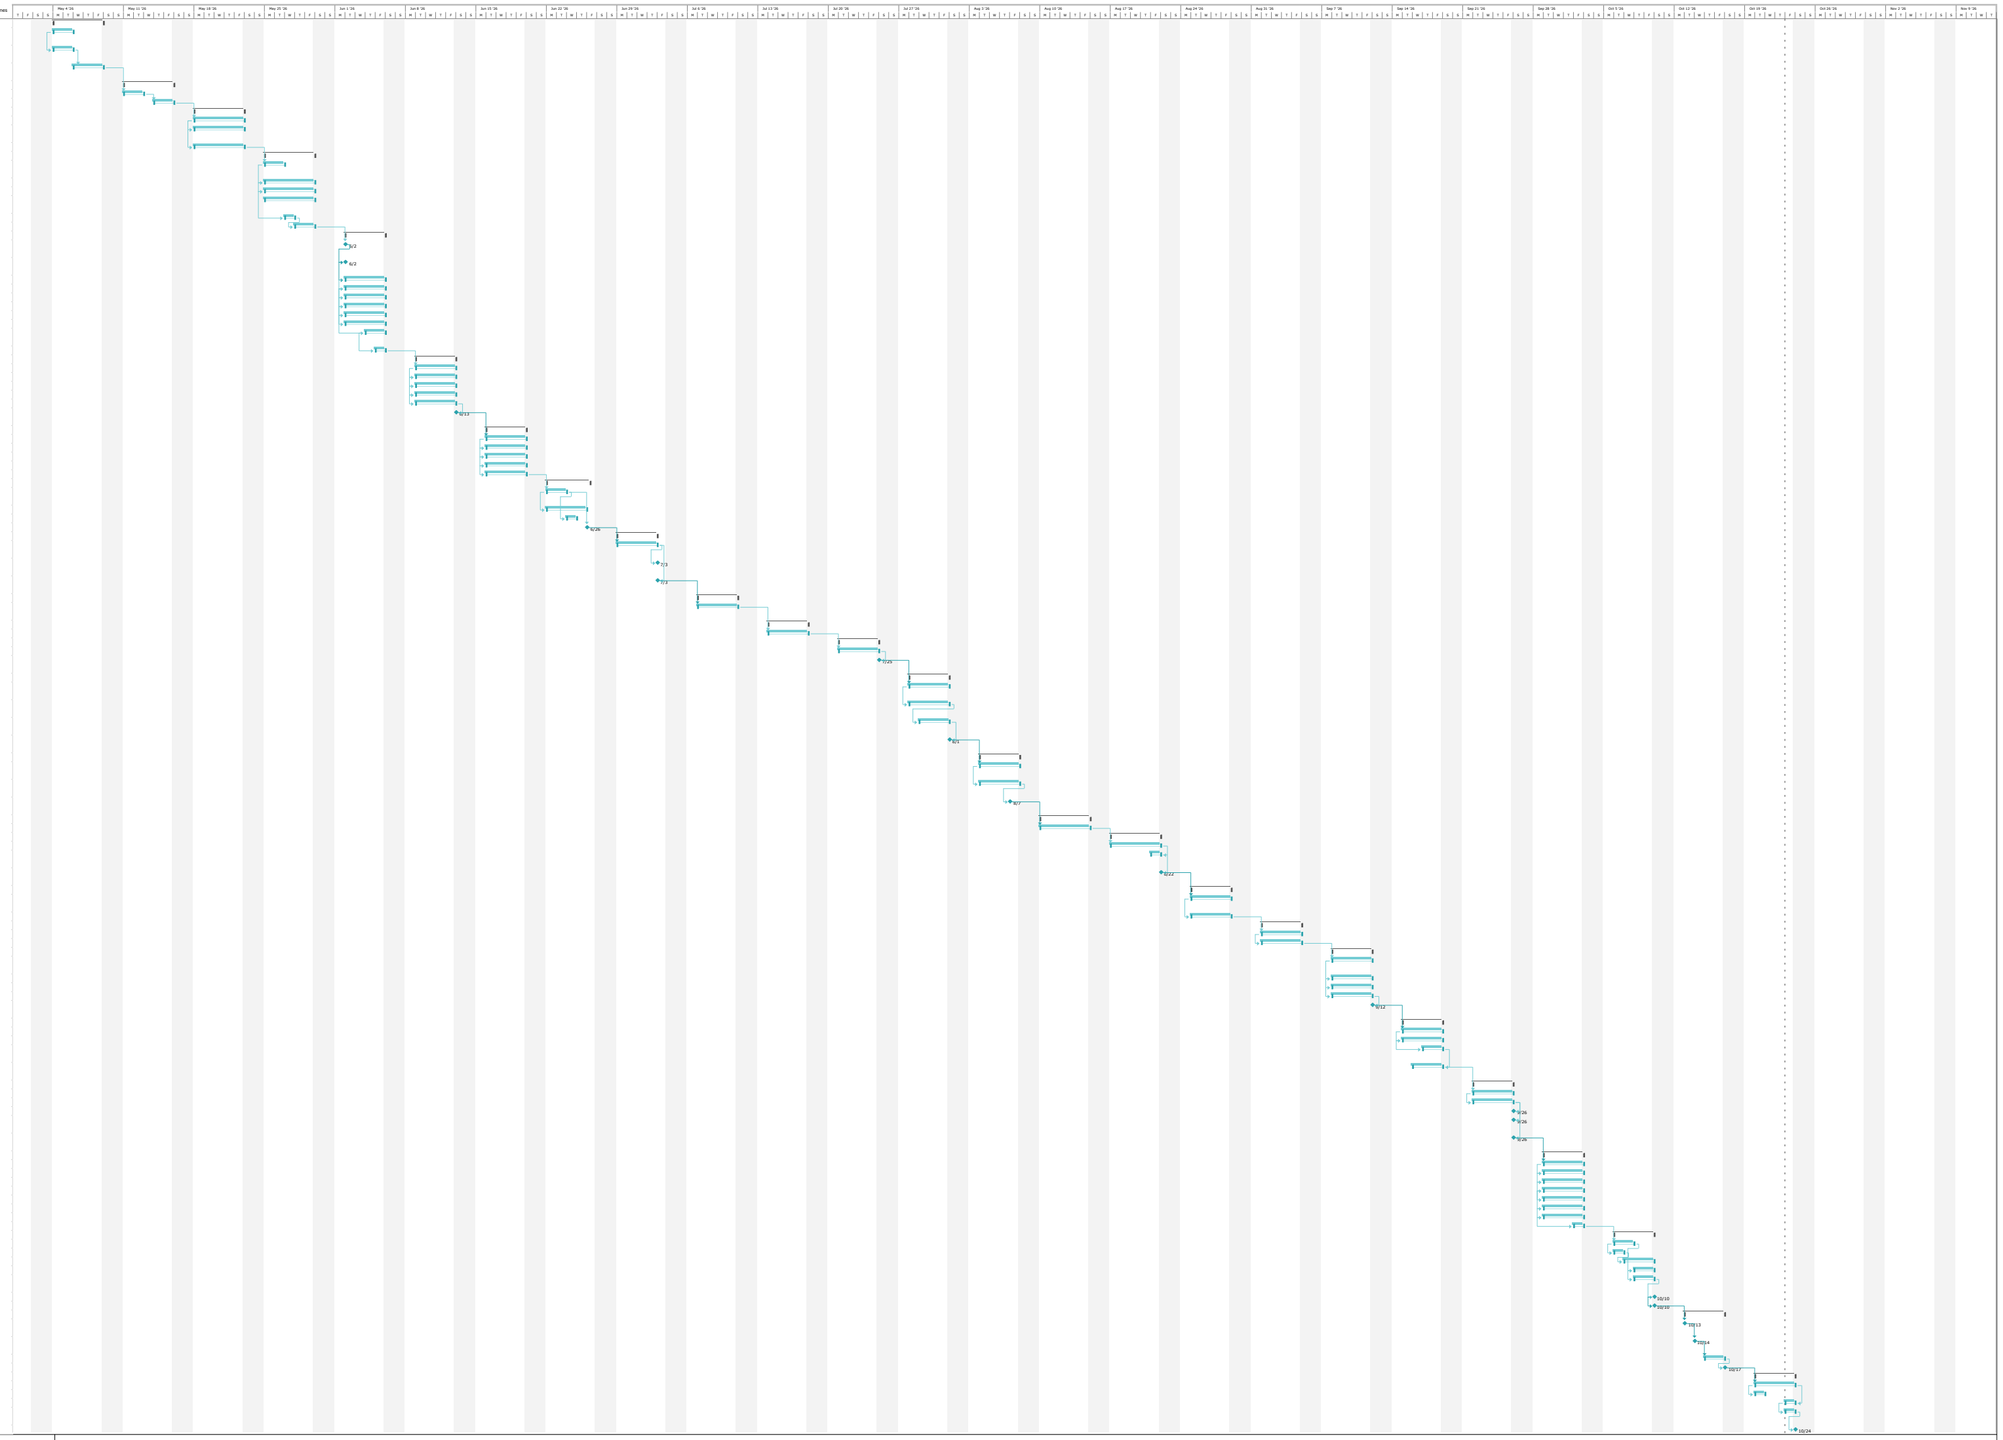

Project: Copley Apartments Retail
Date: Wed 4/29/26 9:36 AM

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress

Celine Aventura Mall

Weekly Construction Schedule Summary · May 4 – Oct 23, 2026 · Project Manager: Shawn Rasmusen

Phase	Wk	Dates	Activities
Site Prep	1	May 4 – 8	Site verification of existing conditions · Create floor verification plan for level · Level or grind floor as required
Site Prep	2	May 11 – 15	Complete floor level · Store layout
Rough-In Start	3	May 18 – 22	HVAC rough · Storefront heavy gauge framing · Electrical/LV rough
Rough-In Start	4	May 25 – 29	Air handler delivery and installation · HVAC rough · Electrical/LV rough · Wall framing/blocking · Scan and trench · Plumbing rough
MEP Rough-In	5	Jun 2 – 5	Delivery of Light troughs · Delivery and install of speakers · Framing/Blocking · HVAC rough · Electrical/LV rough · Plumbing rough · Sprinkler rough · FA rough · Trench rough inspection · Trench infill
MEP Rough-In	6	Jun 9 – 12	Framing/Blocking · HVAC rough · Electrical/LV rough · Sprinkler rough · FA rough · Delivery of Smart Meter
MEP Rough-In	7	Jun 16 – 19	Framing/Blocking · HVAC rough · Electrical/LV rough · Sprinkler rough · FA rough
Inspections	8	Jun 22 – 25	MEP rough inspections · Framing/Blocking · HVAC balance · Framing inspection
Drywall	9	Jun 29 – Jul 2	Drywall install on walls · Level 5 drywall sample completed · Delivery of knife edge cover connectors
Drywall	10	Jul 7 – 10	Drywall on walls and ceilings
Drywall	11	Jul 14 – 17	Drywall finishing
Drywall	12	Jul 21 – 24	Drywall Finishing · Delivery of Basalite tile
Finishes	13	Jul 27 – 31	Storefront installation · Interior paint and prime · Install interior HM doors · Dry layout of FOH tile with client
Finishes	14	Aug 3 – 7	Storefront installation · Interior paint and prime · Install BOH ACT ceilings
Tile & Floor	15	Aug 10 – 14	FOH tile installation
Tile & Floor	16	Aug 17 – 21	FOH tile installation · Install Floor protection · Resense ceiling and floor light delivery
Millwork	17	Aug 25 – 28	Storefront facade install Millwork team · Millwork installation
Millwork	18	Sep 1 – 4	Millwork installation · Millwork electrical
Millwork	19	Sep 8 – 11	Storefront facade install Millwork team · Millwork installation · Electrical Millwork · BOH Millwork install · Delivery of LV rack, WAPS, Ect
Millwork	20	Sep 14 – 18	Millwork installation · Electrical Millwork · Delivery and install of Mobile shelving and lockers · Delivery of BOH appliances
Millwork	21	Sep 21 – 25	Millwork installation · Electrical Millwork · Delivery of safe · Delivery of People Counter · Delivery of EAS/security
Fit-Out	22	Sep 28 – Oct 2	Millwork Punch · Electrical Millwork · IT installation · Audio install · Security install · Plumbing fit out · Sprinkler fit out · Intertek inspection
Punch & Inspect	23	Oct 5 – 9	Final Paint touchups · GC punch visit · GC punch list items · Final Clean #1 · Exterior signage installation · MEP final inspections · Signage inspection
Final Inspect	24	Oct 12 – 16	Life Safety Inspection · Final Building inspection · Final Clean #2 · Client turnover
Stocking & Open	25	Oct 19 – 23	Stock Store · Install Dishwasher · Remove barricade · Touch up for barricade removal · Store Opening

*Final turnover: **Friday, October 23, 2026** · See attached Gantt chart for detailed dependencies and milestones.*
